

Dear Neighbour

Please find below an update on the works that will taking place over the next week.

50 Jermyn Street

- Commence preparation work to existing vault slab to allow connection of the new Ground Floor slab
- Delivery of slipform elements

180 Piccadilly

- Complete Demolition of Ground Floor Slab
- Continue with the breaking out and removal of basement slab
- Excavate to formation level of new basement slab and commence waterproofing works
- Cast basement foundation slab along link block building and commence assembly of slipform rig
- The breaking out of the slab will be along the party line in the Northwest Corner (Piccadilly Street/ Adjacent to the Arcade)

Client: GPE


Contractor: Mace

Start of Works: November 2024

Estimated Completion: Summer 2026


Site Hours:

Monday to Friday 8:00am to 6:00pm
Saturday 8:00am to 1:00pm

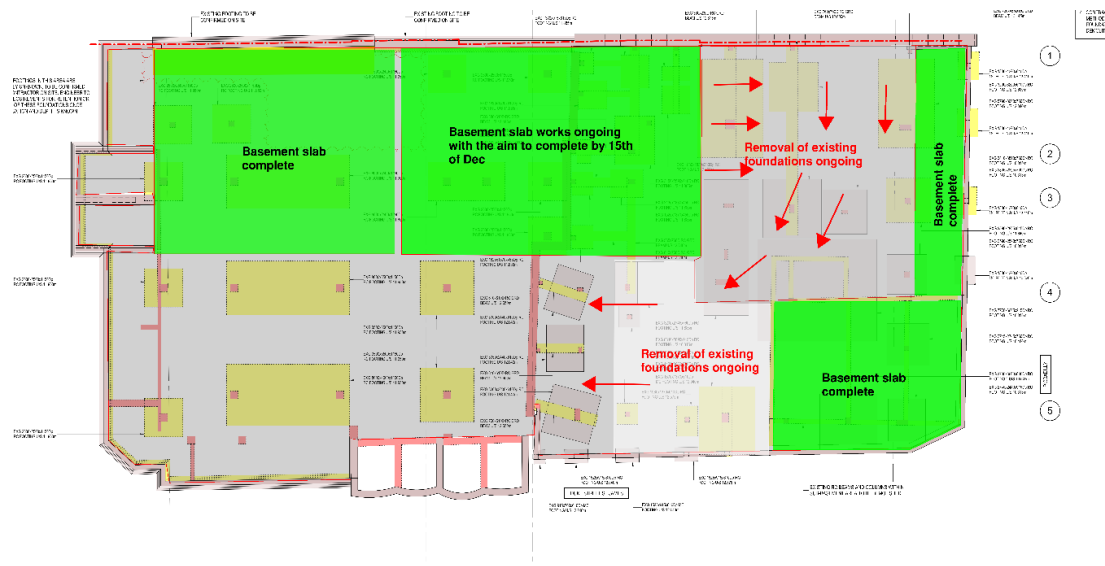

Day of the week	Noisy works carried out		
	08:00 – 10:00	12:00 – 14:00	16:00 – 18:00
Monday	Breaking out of basement slab	Breaking out of basement slab	Breaking out of basement slab
Tuesday	Breaking out of basement slab	Breaking out of basement slab	Breaking out of basement slab
Wednesday	Breaking out of basement slab	Breaking out of basement slab	Breaking out of basement slab
Thursday	Breaking out of basement slab	Breaking out of basement slab	Breaking out of basement slab
Friday	Breaking out of basement slab	Breaking out of basement slab	Breaking out of basement slab
Saturday	No noisy activities	No noisy activities	No activity on site
Sunday	No activity on site	No activity on site	No activity on site

Please see below 5 months look ahead

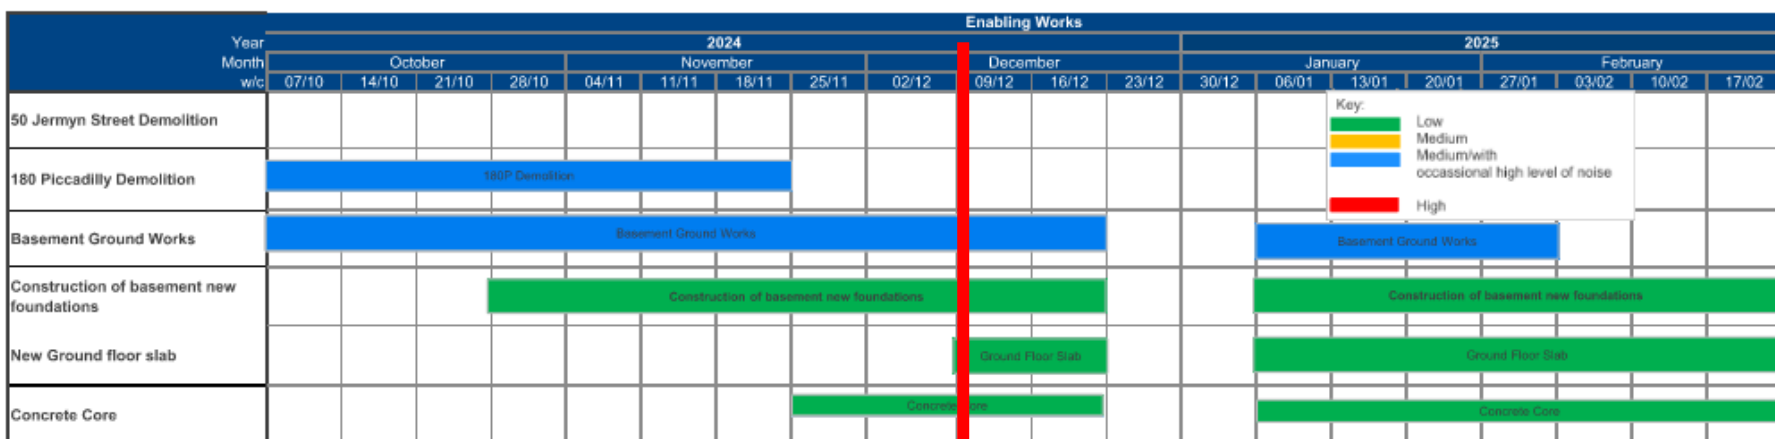

SITE CONTACT DETAILS

If you have any queries or suggestions, please contact your site team using the details below



Suzanne Hardy
Neighbour Liaison Manager
07794 247622
Suzanne.hardy@macegroup.com



Seanin Hegarty
Construction Lead
07887 655073
Seanin.hegarty@macegroup.com

THE CONSTRUCTION TEAM



Sal Capotosto
Project Director



Pippa Hill
Construction Management Graduate



Nicholas Bull
Senior Project Manager



Ayeisha Khalifa
Project Management Apprentice

You can also visit the 180 Piccadilly Construction website at <https://www.180piccadilly.construction> for further details about the project.

In a site-based emergency please call the site team
